


Software Engineering

Lab 2: Agile Backlog Creation & Sprint Simulation in Jira

Name: Puneeth Yenneti SRN: PES1UG24CS348 Section: F

Deliverables


Screenshot1: Epics

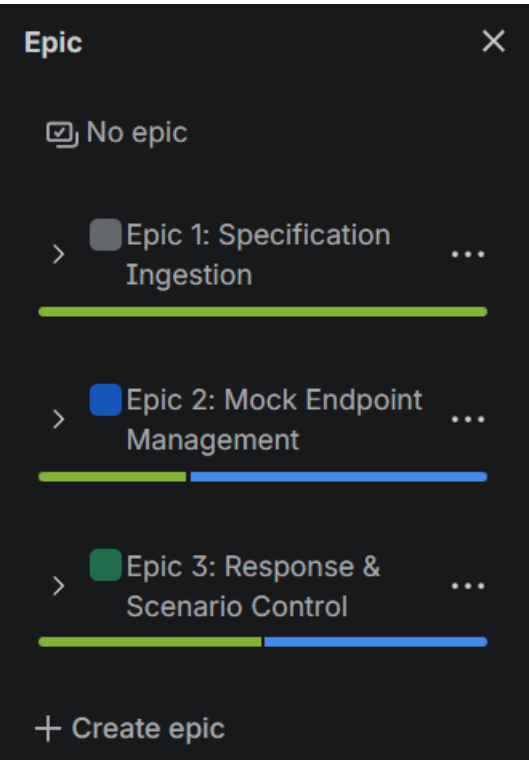

Screenshot 2: Story Points

☐	▼	OMSG Sprint 1 2 Sep – 9 Sep (7 work items)		0	13	21	Complete sprint	...
☒	OMSG-4	Story 1.1 — Upload Specification	☐ Epic 1: Sp...	Done ▼	5	^	👤	
☒	OMSG-5	Story 1.2 — Spec Validation Feedback	☐ Epic 1: Sp...	Done ▼	3	=	👤	
☒	OMSG-9	Story 3.1 — Configure Response Latency	☒ Epic 3: Re...	Done ▼	5	^	👤	
☒	OMSG-6	Story 2.1 — Generate Mock Endpoints	☒ Epic 2: M...	Done ▼	8	^^	👤	
☒	OMSG-8	Story 2.3 — View Mock Server Logs	☒ Epic 2: M...	In Progress ▼	3	=	👤	
☒	OMSG-7	Story 2.2 — Request Schema Validation	☒ Epic 2: M...	In Progress ▼	5	=	👤	
☒	OMSG-10	Story 3.2 — Switch Response Scenarios	☒ Epic 3: Re...	In Progress ▼	5	=	👤	

Screenshot 3: Active sprint (done in only one sprint)

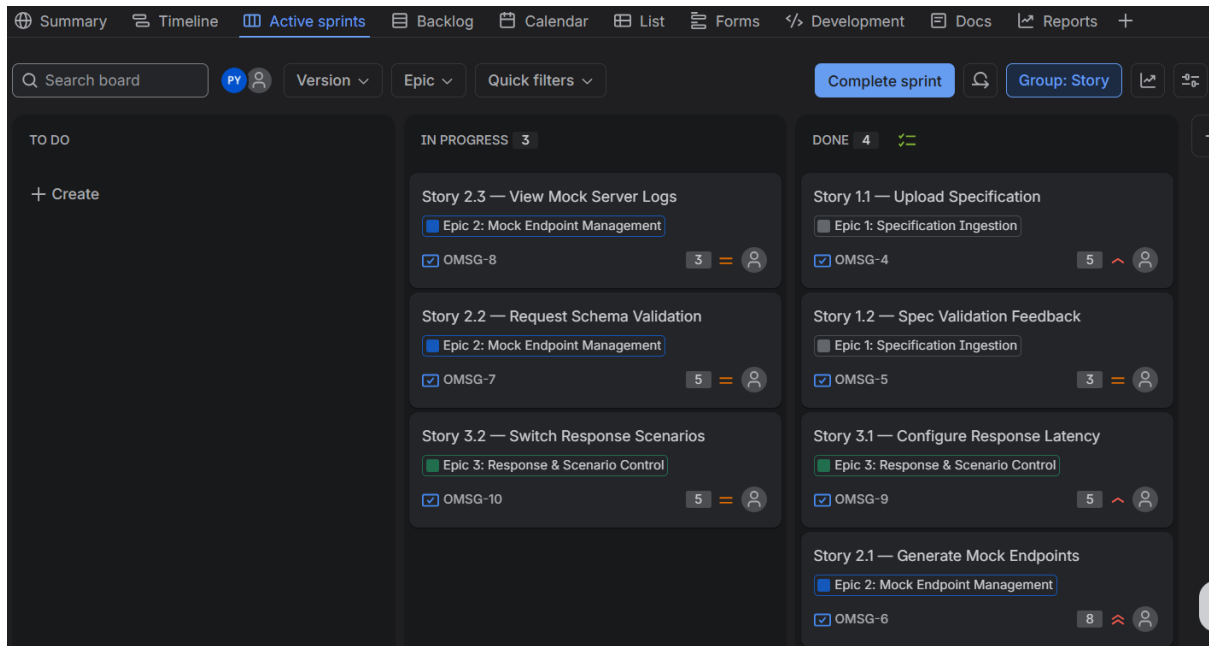

Screenshot 4: Burndown Chart



Reflection Questions

1. Did your estimations reflect the actual effort?

Ans: Largely yes— the sprint completed all stories within the timebox. However, the spike mid-sprint was due to adding tasks to the sprint which were not added to it initially. The sudden spike followed by a steep drop also indicates that tasks were

moved to Done in bulk rather than gradually, which is typical of a simulated sprint rather than real incremental delivery.

2. Was your backlog well-prioritized?

Ans: Yes - high-priority items were included in the sprint 1 first. The backlog was structured around two actors i.e., API Developer and QA Engineer, which kept stories logically grouped and easier to prioritize by user impact.

3. How did your simulated sprint align with your plan?

Ans: The sprint mostly aligned with the plan — all story points were burned by the end of the sprint window. The main deviation was the scope increase on Sep 7, which added roughly 13–14 points mid-sprint. Despite this, the team (simulated) was able to complete everything, suggesting the original velocity estimate of ~19 points may have been conservative.

4. What insights did the burndown chart give about your team's capacity?

Ans: The chart shows the team can handle around **19–21 story points** per sprint at a comfortable pace. The flat line during non-working days (Sep 5–6) confirms no work was done on weekends, which is realistic. The sharp drop on Sep 7–8 rather than a gradual burn is the most notable insight — in a real team this would indicate work is being completed in bursts, which is a risk pattern called "*last-minute completion*." It may signal that stories should be broken into smaller subtasks to encourage steadier daily progress.
